ID	% Complete	Task Name	Duration	Start	Finish
1	**79%**	**ROCKER REDESIGN PROJECT**	**75 days**	**Mon 8/28/23**	**Fri 12/8/23**
2	**96%**	**1. DOCUMENTATION**	**25 days**	**Mon 8/28/23**	**Fri 9/29/23**
3	100%	1.1. Project Proposal	8 days	Mon 8/28/23	Wed 9/6/23
4	100%	1.2. Responsibility Assignments	1 day	Mon 8/28/23	Mon 8/28/23
5	95%	1.3. Load Testing Plan	25 days	Mon 8/28/23	Fri 9/29/23
6	**100%**	**2. SIMULATION**	**5 days**	**Mon 10/2/23**	**Fri 10/6/23**
7	100%	2.1. Complete Static Analysis	5 days	Mon 10/2/23	Fri 10/6/23
8	100%	2.2. Complete Dynamic Analysis	5 days	Mon 10/2/23	Fri 10/6/23
9	**100%**	**3. MANUFACTURE PARTS**	**14 days**	**Tue 11/7/23**	**Fri 11/24/23**
10	100%	3.1. Secure Material (PA6-CF)	14 days	Tue 11/7/23	Fri 11/24/23
11	100%	3.2. Manufacture Front and Rear Rockers	14 days	Tue 11/7/23	Fri 11/24/23
12	**33%**	**4. TEST AND ANALYZE ROCKERS**	**29 days**	**Mon 10/30/23**	**Thu 12/7/23**
13	100%	4.1. Obtain Load Testing Plan Approval	1 day	Mon 10/30/23	Mon 10/30/23
14	100%	4.2. Secure Test Rig	10 days	Tue 11/7/23	Mon 11/20/23
15	0%	4.3. Perform Cyclic Testing and Record Data	20 days	Tue 11/7/23	Mon 12/4/23
16	0%	4.4. Revise Initial Data and Testing Methods	2 days	Tue 12/5/23	Wed 12/6/23
17	25%	4.5. Analyze New Data	1 day	Thu 12/7/23	Thu 12/7/23
18	**100%**	**5. REPORT AND PRESENTATION**	**4 days**	**Tue 12/5/23**	**Fri 12/8/23**
19	100%	5.1. Create Project Report	4 days	Tue 12/5/23	Fri 12/8/23
20	100%	5.2. Create Project Presentation	2 days	Tue 12/5/23	Wed 12/6/23

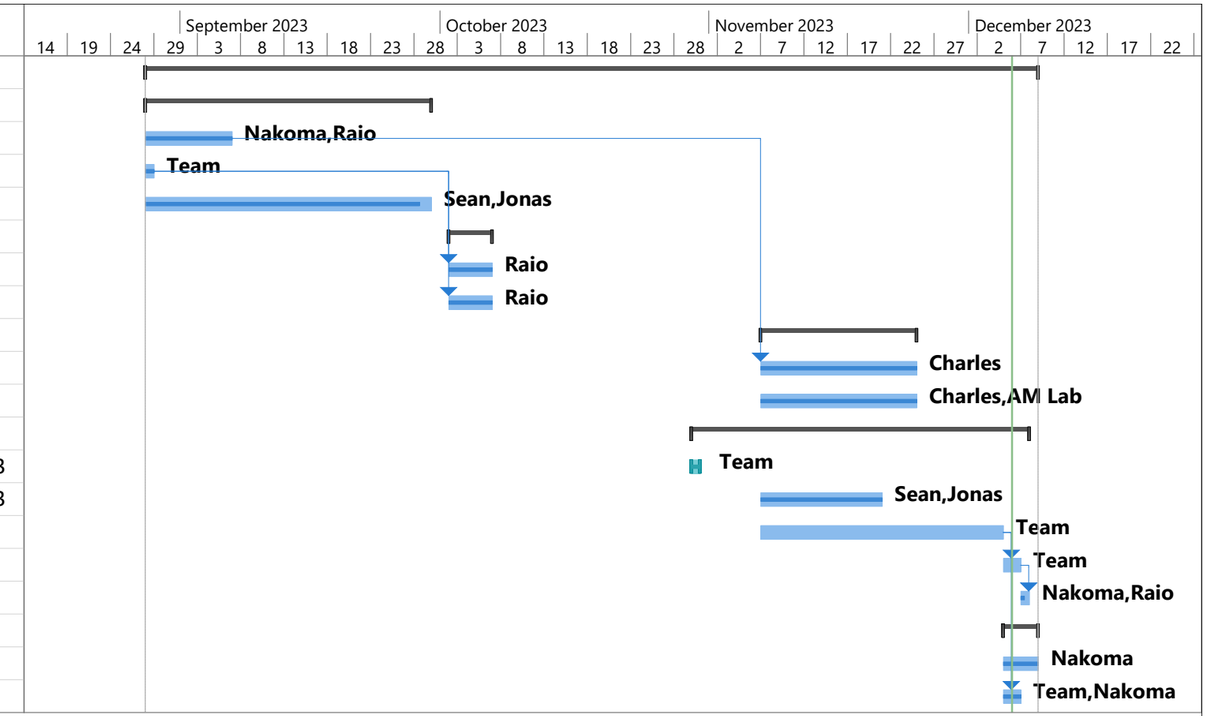

Project: MAE435-GANTT
Date: Wed 12/6/23

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
